# VENDOR DOCUMENTS

# HANDLING PROCEDURE

# FOR

# ONSHORE FACILITY

**CONTRACT NO.** : **POGC-760-81-156**

**PROJECT** : **SOUTH PARS GAS FIELD DEVELOPMENT (PHASES 9&10)**

**COMPANY** : **NATIONAL IRANIAN OIL COMPANY**

**SITE** : **ASSALUYEH / SOUTH PARS GAS FIELD PERSIAN GULF, IRAN**

| | | | | | | | |
|---|---|---|---|---|---|---|---|
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| B | 12/06/2003 | Reflected OIEC's comments | LG | CSY | HSK | | KSL |
| A | 24/03/2003 | Issued for OIEC Review | LG | CSY | HSK | | KSL |
| **REV.** | **DATE** | **DESCRIPTION** | **ORIG.** | **PRPD** | **CHKD** | **APP'D** | **Contractor's APP'D** |

# CONTENTS

1. General
1.1 Intent
1.2 Scope
1.3 Definitions
1.4 Project Descriptions
1.5 Address of PURCHASER for Documents Transmittals
1.6 Correspondence Numbering

2. Documents to be submitted
2.1 Vendor Documents to be submitted
2.2 General Requirements
2.3 Number of Copies to be Submitted and Required Issue Schedule

3. Documentation Procedure
3.1 Document Title and Stamps
3.2 Standard Forms
3.3 Numbering of Vendor Documents
3.4 Revision or Modification on Vendor Documents
3.5 As-Built Drawings
3.6 Vendor Data Book
3.7 Electronic Data File

Attachment - 1 : Vendor Documents Issue Schedule
Attachment - 2 : Vendor Documents Transmittal Procedure
Attachment - 3 : Standard Forms

# 1. General

## 1.1 Intent

This document specifies documentation procedures for documents and drawings (hereafter collectively called as "Vendor Documents") to be prepared and submitted by VENDOR, for the South PARS GAS FIELD DEVELOPMENT (PHASES 9 & 10) PROJECT (hereafter called "SP 9&10 PROJECT").

## 1.2 Scope

This document applies to Vendor Documents to be prepared and submitted by VENDOR except for correspondence and commercial data to CONSORTIUM.

For documents for quality assurance, inspection and tests, packing and shipping, schedule/status control and spare parts and interchangeability record (SPIR), shall be applied.

## 1.3 Definitions

| | | |
|---|---|---|
| COMPANY | : | means National Iranian Oil Company or POGC(Pars Oil & Gas Company) and shall include its representatives, successors and permitted assigns. |
| CONSORTIUM | : | means Consortium of LG Engineering & Construction Corporation (hereafter called "LGE&C") and Oil Industries Engineering & Construction (hereafter called " OIEC") and shall include its representatives, successors and permitted assigns. |
| PURCHASER | : | means a party of CONSORTIUM who issues Purchase Order to VENDOR under the name of CONSORTIUM. |
| VENDOR | : | means any vendor/supplier who will supply equipment, materials etc. under Purchase Order for SP 9&10 Project. |

## 1.4 Project Descriptions

| | | |
|---|---|---|
| COMPANY | : | National Iranian Oil Company or POGC(Pars Oil & Gas Company) |
| Project Name | : | South Pars Gas Field Development (PHASES 9&10) |
| Plant Location | : | Assaluyeh, Iran |
| Consortium Work No. | : | POGC-760-81-156 |

### 1.5 Address of PURCHASER for Documents Transmittals

VENDOR shall submit Vendor Documents to the responsible party of CONSORTIUM based on the ATTACHMENT-2. Actual formation within CONSORTIUM and specific requirements for Purchase Order will be advised at the kick-off meeting.

LGE&C

| | | |
|---|---|---|
| Address | : | LG Engineering & Construction Corporation<br>SP 9&10 Project<br>537, Namdaemun-Ro 5-Ga, Joong-Gu, Seoul,<br>100-722, Korea |
| Facsimile number | : | 82-(0)2-728-1220 & 1228 |
| E-mail Address | : | |
| Telephone number | : | |
| Representative | : | |

OIEC


| | | |
|---|---|---|
| Address | : | Oil Industries Engineering & Construction<br>No. 2 Pirooz St., South Kamranieh Ave., 19379<br>Tehran, Iran |
| Facsimile number | : | 98-21-221-5851 |
| E-mail Address | : | |
| Telephone number | : | |
| Representative | : | |

### 1.6 Correspondence Numbering

All entities are required to maintain their own tag to record incoming and outgoing correspondence numbers. All entities will be required to inform others when they find gaps in sequence numbering. The correspondence shall be in English and limited one subject as far as practical.

Dates shall be written in the following order : day, month, year. All correspondences shall principally be signed by and through the authorized Project Manager or Persons who takes charge in this Project.

All Correspondences shall be numbered consecutively




Note 1 : Correspondence Type Code

- "L" for letters
- "F" for facsimile
- "TR" for transmittal
- "E" for E-mail

Note 2 : Sender / Receiver Code

- "LGS" for LGE&C, Seoul, Korea
- "OIT" for OIEC, Tehran, Iran
- XX : Vendor Identification Code
- Y : Location Code
- Vendor Identification Code is to be agreed at the Vendor Kick-Off Meeting.

For example, Vendor's first Fax to LGE&C shall be as follows.

6340S - XXX / LGS - 001 - F

## 2. Documents to be submitted

Vendor Documents shall contain comprehensive detail information of design and engineering, manufacturing and fabrication, inspection and tests, packing and shipping, installation, operation, maintenance, and monitoring of progress status.

VENDOR shall submit applicable Vendor Documents as listed in para 2.1 as a minimum and other documents/drawings required under PURCHASER's Requisition and/or applicable specifications.

### 2.1 Vendor Documents to be submitted

The detail requirements for Vendor Documents for the respective item will be respectively specified in each Requisition. The followings are typical requirements for Vendor Documents.

a) Vendor Print Index and Schedule (Refer to para. 3.2 for details)

- Vendor Print Control Sheet
- Vendor Print Index & Schedule

b) Technical Documents and Drawings such as;

- Equipment Data Sheet
- Equipment Description
- Equipment Inventory
- Connection Parameter (Piping, Electrical & Instrument)
- Control Loop Diagram
- Performance Guarantee Information including Performance Curve
- Strength Calculation
- Stress Analysis Report, if required
- Assembly Drawing
- Sectional Drawing
- Process / Utility Flow Diagram
- P&I Diagram
- Layout Drawing / Plot Plan
- Piping Drawing
- Instrument Index
- System Application Program Software with License
- Control Panel / Gauge Drawings
- Wiring Diagram for Instrumentation and Electrical system

- Equipment Loading Data for Civil Design
- Calibrated Equipment Loading Data
- Motor Data Sheet / Characteristic Curve
- Utility and Chemical Consumption Data
- Lubricants List
- Calculation Notes
- Effluent Summary
- Logic Diagram
- Cause & Effect Chart
- Line List
- Noise Data Sheet
- Catalogs

c) Manual/Procedures

-QA / QC Manual
- Quality Assurance Plan
- Welding, PWHT Procedure for Site Assembling Work
- Fabrication Procedure
- Inspection and Test Procedure with Plan
- WPS & PQR with welding Joint Map
- Welding Repair Procedure
- Welders Qualification Test Report
- NDT Procedure with NDT Map
- PWHT Procedure
- Painting Application Procedure
- Protection and preservation Procedure (for long term storage)
- Procedures for Erection, Pre-commissioning, Commissioning & Start-up
- Installation Manual with Assembling Procedure
- Detail Sequence Diagram of Site Assembling for Package Item
- Operation Manual including Operating Procedure, On-line Monitoring, First level Maintenance by Operators and Lubrication Schedule
- Maintenance Manual including Scheduled Inspections or Interventions, Preventive On-failure and Overhaul Maintenance Procedure including Description of Personnel, Tools, Spare Parts, Drawings required, Trouble Shooting Charts, List of Consumables.

d) Spare Parts List and Special Tools List

- Spare Parts and Interchangeability Records (SPIR)
- Special Tools List
- Insurance Spares
- Construction / Pre-commissioning Spares
- Commissioning / Start-up Spares
- Two years Operational Spares

e) Inspection and Test Records / Certificates

f) Certificates
- Material Certificate
- Inspection Release Certificate
- Certification Authority Inspection Release Note, where applicable
- The letter of Certificate of Conformity with Purchase Order

- Material Test Certificate

g) Packing List and Documents for Shipping

h) Overall Fabrication Schedule / Monthly Progress Report

i) Vendor's Personnel / Organization

j) Sub-vendor List

k) Minutes of Meeting

**2.2 General Requirements**

1) All Vendor Documents to be submitted by VENDOR shall be specified with ;

| | |
|---|---|
| Consortium Work No. | : POGC-760-81-156 |
| Project Name | : South Pars Gas Field Development (Phases 9 & 10) |
| PURCHASER Req. No. | : (See Requisition) |
| Item No. | : (See Requisition) |

2) Language
All Vendor Documents shall be written in English language.

3) Document Size and Quality
Vendor Documents to be submitted shall be made in the following standard sizes;

| Type | Size in mm |
|---|---|
| A(A4) | 210 x 297 |
| B(A3) | 297 x 420 |
| C(A2) | 420 x 594 |
| D(A1) | 594 x 841 |
| E(A0) | 841 x 1189 |

4) Vendor Documents prepared by VENDOR shall be sent to CONSORTIUM via courier in compliance with VENDOR DOCUMENTS TRANSMITTAL PROCEDURE in ATTACHMENT-2, unless otherwise specified.

5) The Unit applied to the Vendor Documents shall be as follows ;

Metric and Celsius unit except for piping size and rating which confirm to inch and pound system.

**2.3 Number of Copies to be Submitted and Required Issue Schedule**

The number of copies of Vendor Documents and due date of each document/drawing shall be as per ATTACHMENT-1.

## 3. Documentation Procedure

### 3.1 Document Title and Stamps

All Vendor Documents to be submitted shall have the title block and identification stamp as specified below:

1) Title Block for SP 9&10 Project

Title Block shall be indicated on cover sheet of every document. In case of drawing, Title Block shall be located at right below on the every drawings. Standard Title Block for SP 9&10 Project in the form of label will be provided by PURCHASER

| | | | | | | | |
|---|---|---|---|---|---|---|---|
| | | | . | | | | |
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| | | | | | | | |
| A | 20/02/03 | Issued for OIED/IOEC Review | | | | | |
| Rev. | Date | Description | ORIGI | PRPD | CH'D | APP'D | Contractor Approved |

**SOUTH PARS GAS FIELD DEVELOPMENT – PHASES 9&10, ASSALUYER – IRAN ONSHORE FACILITIES**

N.I.O.C Pars Oil & Gas Company

| Project No. : POGC-760-81-156 | Doc. Class : | Scale : |
|---|---|---|
| FEED COMPANY LOGO | OIEC | IOEC |

UNIT 100 : RECEIPTION FACILITIES
PRESSURE LETDOWN STATION
PIPING AND INSTRUMENT DIAGRAM

| DRAWING No. | | SHT No. | of | Rev. 0 |
|---|---|---|---|---|

Note : This document is a property of NIOC and cannot be copied and handed to Third Party without Client's authorization.

CAD Reference No. :

Note 1 : Vendor Logo, Req. No. and Item No. shall be filled in by VENDOR.
Note 2 : The sizes of title block for the respective drawing are as below. The height and width of the respective title block are same in principally.
- A0 & A1 : 150 mm
- A2 : 130 mm

- A3 : 95 mm
- A2 : 74 mm

2) Stamping

Every Vendor Documents shall be stamped(width:70 mm / height:15 mm) with one of the following descriptions to indicate the status of each document;

a) Document/drawing issued for “FOR APPROVAL”

**FOR APPROVAL**

b) Document/drawing issued for “FOR FINAL” prior to “FINAL” issue.

**FOR FINAL**

c) Document/drawing issued as “FINAL”

**FINAL**

d) Document/drawing issued as “AS-BUILT”

**AS-BUILT**

e) Document/drawing issued for “FOR INFORMATION”

**FOR INFORMATION**

e) Document/drawing issued for “FOR REVIEW”

**FOR REVIEW**

### 3.2 Standard Forms

Documents listed below shall be submitted using Standard Form for SP 9&10 Project as shown in ATTACHMENT-3 :

1) Vendor Print Control Sheet (VPCS) (Form 1)

VENDOR shall submit a transmittal cover sheet in attached Form 1 with main documents for CONSORTIUM's filling it up.

The transmittal cover sheet and main documents will be returned with specifying CONSOTRTIUM's check results on VPCS using the following codes :

a) CODE 1 (Approved without Comments) : Vendor to submit "FINAL"

b) CODE 2 (Approved with Comments) : Vendor to amend and submit "FINAL"

c) CODE 3 (Approved with Comments) : Vendor to amend and submit "FOR APPROVAL"

d) CODE 4 (Unacceptable Quality) : Vendor to re-submit

Note : The above checking results by CONSORTIUM shall in no way relieve VENDOR of any liability, obligation and responsibility out of the Purchase Order and the mutual agreement in writing.

2) Vendor Print Index and Schedule (VPI) (Form 2)


VENDOR shall submit this form listing all Vendor Documents with their issue schedule.

VENDOR shall submit VPI duly filled in together with the specified documents(Form 3) within two weeks after the Purchase Order or award commitment.
(Refer to ATTACHMENT-2 for details)

3) Overall Manufacturing Schedule / Detail Production Schedule (Form 3)
4) Sub-order Status Report (Form 4)
5) Vendor Personnel/Organization (Form 5)
6) Monthly Progress Reports (Form 6)
***7) Electric Load List (Form 7)***
***8) Lubricant List (Form 8)***
***9) Utility Consumption List (Form 9)***
***10) SPIR Format (Form 10)***
***11) Special Tool List (Form 11)***


### 3.3 Numbering of Vendor Documents

1) For General Common Document
(such as Specification, Inspection & Tests Procedure, Reports and Lubricants List, etc.)

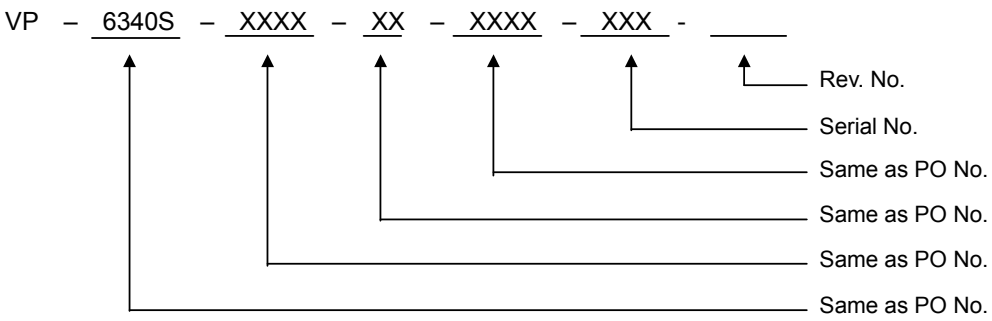


For example, in case of Equipment with PO-6340S-0800-LG-0001, Common Vendor Document Number pertaining to the Purchase Order shall be as follows;
VP-6340S-0800-LG-0001-XXXX (serial No)-Rev.0

2) For Individual Document & Drawing for Each Item

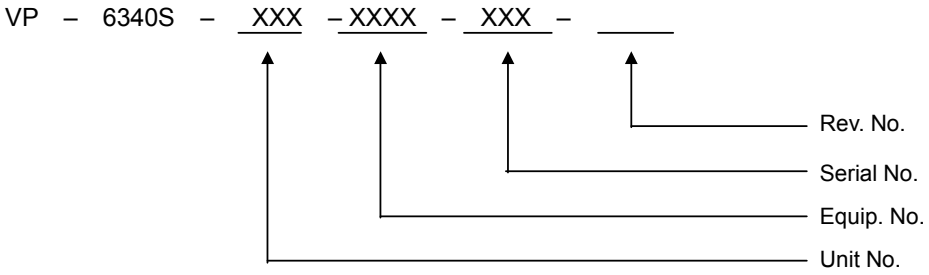


For example, in case of Equipment with PO-6340S-1000-OI-0005, Vendor document number for Refrigerant Compressor (111-K-101) in unit 111 shall be as follows;
VP-6340S-111-K101-XXXX-Rev.0

**3.4 Revision or Modification on Vendor Documents**

1) All Vendor Documents shall be indicated with revision number to indicate the revision status of each document/drawing. When any revision or modification is made, a subsequent revision number shall be indicated and previous revision marks shall be removed form the documents and drawings.

2) History of revision / modifications shall be recorded by VENDOR, and the records shall be accompanied with concerned documents/drawings as “Revision History”

3) The area in the documents/drawings where a revision or modification was made shall be indicated and highlighted with revision marks by a cloud.

**3. 5 As-Built Drawings**

In case that any one in documents/drawings listed in the Para. 2.1 is included in VENDOR’s scope of submission and any modification(s)/revision(s) will be occurred due to the actual situation at site during construction/erection, precommissioning and commissioning of the plant, VENDOR shall prepare and submit “As-Built” revision of Vendor Documents to CONSORTIUM without any additional cost, based on the marked-up documents/drawings provided by CONSORTIUM.

**3. 6 Vendor Data Book**

VENDOR shall submit the Vendor Data Book in accordance with the following Procedure;

1) “Index” submission for Vendor Data Book
VENDOR shall submit the details of the format and contents of the Vendor Data Book to the CONSORTIUM for APPROVAL prior to starting preparation.

2) “FOR APPROVAL” submission of Vendor Data Book
After getting CONSORTIUM’s confirmation on Index in above article 1) without any comments, Vendor shall submit 5 copies of Vendor Data Book to CONSORTIUM for APPROVAL before shipping goods.

3) “APPROVED” submission of Vendor Data Book
If the Vendor Data Book in above article 2) are approved by CONSORTIUM, VENDOR shall finally submit the **Vendor Data Book** with stamp of “FINAL” on the first page including electronic files not later than three(3) weeks after shipping of goods as follows;
- 7 full “hard” copies in book
- 12 sets of CD ROMs containing all documents and drawings under ACROBAT “PDF” format
- 12 sets of CD ROMs under original file formats (AUTOCAD 14, OFFICE, etc…)

The Vendor Data Book shall be composed of 3 parts as below.
- Part-I : Design and Manufacturing Document
- Part-II : Operation & Maintenance Manual
- Part-III : Quality Assurance

### 3.6.1 Design and Manufacturing Document (Part-I of Vendor Data Book)

Design and Manufacturing Document of Vendor Data Book shall include followings, but not limited to.

a) Assembly and general layout drawings
b) Sectional Drawings
c) Performance and Test curves
d) Data sheets for main and auxiliary mechanical, instruments and electrical equipment
e) Instrument Wiring Connection and Logic Diagram
f) Details of nozzles, bolts, gaskets and internal attachments
g) Strength calculations and stress analysis report of equipment and / or materials
h) Mechanical seal & coupling drawings
i) Data sheets and drawings for Motor and drivers
j) Instrument Schedule
k) Wiring Diagrams for Instrumentation and Electrical System
l) Equipment Loading Data for Civil Design
m) Welding Procedure Specification (WPS) and Procedure Qualification Record (PQR)
n) Lubricant and utility consumption lists for equipment
o) Installation and operation Procedure
p) Sub-vendor List
q) Unpriced purchase orders indicating purchaser's order reference, vendor's address including those of sub-vendor and place of manufacture and a complete list of all items order.
r) Packing List

All of the aforementioned documents shall represent the as-manufactured state of the item. If any modifications have been made by the VENDOR in the field, such changes shall be incorporated into the appropriate document.

### 3.6.2 Operation & Maintenance Manual (Part-II of Vendor Data Book)

Operation & Maintenance manual shall be in accordance with the followings, but not limited to ;

a) Introduction
b) Description of Systems / Units
c) Preparation prior to Initial Start-up
d) Initial Start-up Procedure
e) Normal Start-up Procedure
f) Normal Operation
g) Normal Shut-down Procedure
h) Emergency Shut-down Procedure
i) Maintenance Procedure
j) Spare Part list for 2 years operation
k) Spare Part & Interchangeability List for 2 years operation
l) Special Tool Lists
m) Appendices

### 3.6.3 Quality Assurance – Inspection Record (Part-III of Vendor Data Book)

VENDOR shall submit QA Record including the inspection record of all inspection items specified in the requisition and engineering specifications.

QA Records shall be submitted to the CONSORTIUM within four(4) days after completion on all inspection and tests.

CONSORTIUM will issue an Inspection Release Notice(IRN) to VENDOR immediately after successful completion of the inspection and tests. The equipment and materials shall not be shipped without IRN.

VENDOR shall submit the booked Inspection Record, which are included in Vendor data book, no later than two(2) weeks after IRN.

### 3.6.4 Bookbinding Procedure for Vendor Data Book

- Note for Filing Works


Documents shall be bound separately per each Requisition No. and Item No. The maximum thickness of book shall be 75mm. If exceed 75mm, it shall be divided into plural books. If it is thin, Document may be bound together with Document of other Item No. of the same Requisition No.

"Final" stamp and documents number shall be put on each Final Documents.

No blue prints shall be allowed to use in the Data Book.

Files shall be for ISO A4 size and durable. If Document is ISO A3 size, it shall be folded to A4 size as "Fig. 3.6.1". If Document is larger than A3 size, it shall be reduced to a size suitable for binding in the Data Book and legible for reading or folded to A4 size and be put into transparent vinyl envelope.

"Fig. 3.6.1"





In case two or more volumes are required for a set of Documents, the first page of each volume must be "individual volume content" which shows only what is included in that volume. The volume no. 1 must contain "all contents" before the "individual volume content".

The cover and back of book shall be furnished in a firmly fashion and the following shall be indelibly printed as shown in "Fig 3.6.2".

(a) P.O No. :
(b) Equipment No. :
(c) Service or Description :
(d) Vol. No. :
(e) Project Name : SOUTH PARS GAS FIELD DEVELOPMENT (Phases 9&10)
(f) COMPANY Name : National Iranian Oil Company
(g) Purchaser's Name : LG Engineering & Construction Co. Oil Industries Engineering & Construction
(h) Vendor Name :

"Fig. 3.6.2"

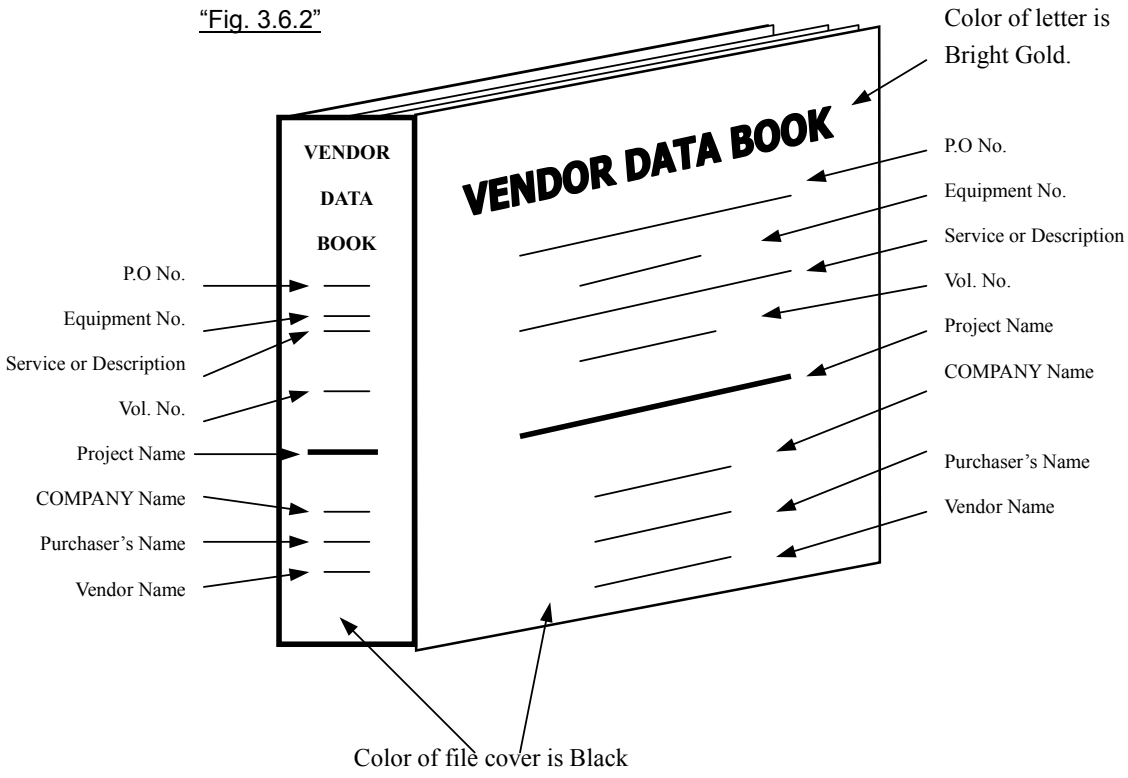


# Note : 1. Thickness of Book : Max. 75mm
2. 4 holes inside to hold papers
3. Cover size : 315 × 280mm (Cover Thickness : 3mm)

## 3.7 Electronic Data File

VENDOR shall submit electronic data files for the following documents/drawings in the following formats with CD storage together with Final Documents and As-Built Drawings.

1) Plot Plans (including Unit/Package Layout Drawing)
2) P&I Diagrams, UFD's and PFD's
3) Foundation Drawings
4) Structural Drawings
5) All drawings for Equipment and machinery (including their internals)
6) Electrical Single Line Diagrams
7) Electrical Drawings
8) Instrument Layouts/Location Drawings
9) Control Panels and Internal Wiring Diagram
10) Underground Piping Drawings
11) Piping Isometrics
12) Plan Drawings of Rack Piping and Offsite Piping

<Format>

| | | |
|---|---|---|
| For drawings | : | Auto CAD Version 14 or higher |
| For documents | : | MS-Word and/or MS-Excel |

**ATTACHMENT-1** **"VENDOR DOCUMENTS ISSUE SCHEDULE"**



| No. | Documents | Quantity to be submitted | | Issue date | Remarks |
|---|---|---|---|---|---|
| | | Hard Copy | CD Storage | | |
| 1. | Vendor Print Control Sheet | 4 | 0 | Every time when submitting Vendor Documents | Standard Form 1 |
| 2. | Vendor Print Index & Schedule | 4 | 0 | Within 2 weeks after Purchase Order or Award commit issue | Standard Form 2 |
| 3. | Documents issued for "FOR APPROVAL" including : Loading Data, Spare Parts List for Erection and Commissioning, Lubricants List, Special Tools List, Utility & Chemical Consumption | 10 | 0 | As per Requisition | |
| 4. | Documents issued for "FOR INFORMATION" or "FOR REVIEW" | 10 | 0 | As per Requisition | |
| 5. | Documents issued for "FOR FINAL" | 10 | 0 | As earliest after Documents were approved or reviewed | |
| 6. | Final Documents | 15 | 2 | Within 2 weeks after final inspection | |


| No. | Documents | Quantity to be submitted | | Issue date | Remarks |
|---|---|---|---|---|---|
| | | Hard Copy | CD Storage | | |
| 7. | Vendor Data Book | As per specified at the Article 3.6 in This procedure. | | 1) Index : before shipping of Material or Goods<br>2) For Approval : Within 2 weeks after shipping<br>3) Approved : Within 2 weeks after Approval of CONSORTIUM | |
| 8. | As-built (If required) | 15 | 2 | Within 2 weeks after VENDOR's receipt of marked-up drawings by CONSORTIUM | |
| 9. | Minutes of Meeting | 3 | 0 | Within 5 days after meeting | |
| 10. | Overall Manufacturing Schedule (Production Schedule) | 3 | 0 | Within 2 weeks after P.O. or Award Commitment | |
| 11. | Vendor's Organization / Personnel | 3 | 0 | Within 1 week after P.O. or Award Commitment | |
| 12. | Subvendors / Suborders List | 3 | 0 | Within 1 month after P.O. or Award Commitment | |
| 13. | Monthly Progress Reports | See Remarks | | As of end of each month should be submitted by 5th of next month. | by fax |
| 14. | Application for Inspection & Test | See Remarks | | At least 2 weeks before inspection | by fax |

**ATTACHMENT-2**

## VENDOR DOCUMENTS TRANSMITTAL PROCEDURE

### 1. VENDOR DOCUMENTS FLOW


After receipt of purchase order or award commitment, VENDOR shall prepare and transmit Vendor Documents according to following flow chart.

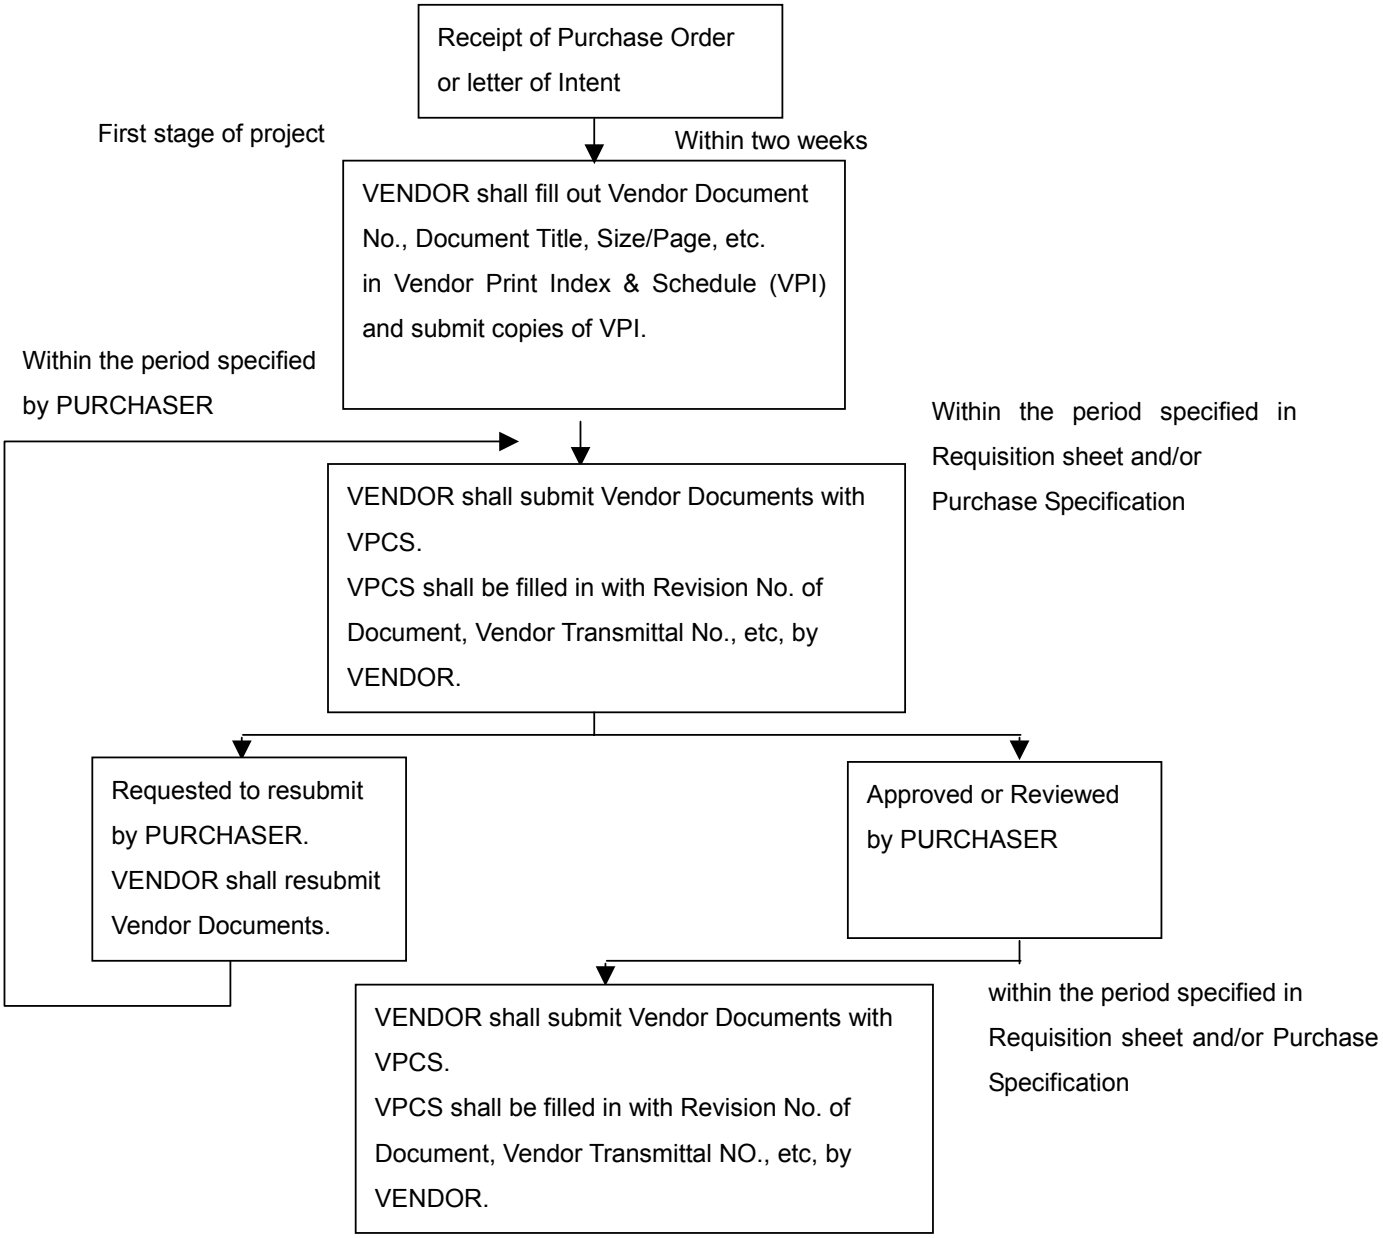

## 2. VENDOR DOCUMENTS TRANSMITTAL AND RETURN

**1) If PURCHASER is LGE&C and Detail Engineering Co. is OIEC (Req. No. : OI*****),**

Documents shall be submitted as follows ;

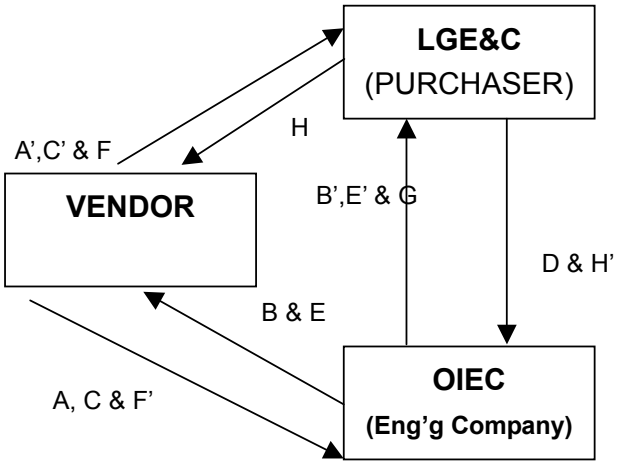


Note :
Inspection Documents include; QC Plan, WPS/PQR, Inspection Procedure, NDE Procedure, Hydrostatic Test Procedure, PWHT Procedure, Manufacturing Data Record (MDR), Fabrication Procedure, and so on

**<Technical Vendor Documents>**

Addressee : OIEC (Detail Engineering Company)
CC : LGE&C(PURCHASER)

A : VENDOR to transmit Vendor Documents to OIEC by courier in compliance with Para. 2.3.

A' : In parallel with A, VENDOR to distribute one (1) copy of Vendor Documents transmitted by A, with VPCS to LGE&C by courier.

B : OIEC to return one (1) copy of Vendor Documents transmitted by A, with CONSORTIUM's checking result to VENDOR by courier. In addition, OIEC to inform VENDOR of COMPANY's comments on these Vendor Documents.

B' : In parallel with B, OIEC to distribute one(1) copy of checked Vendor Documents to LGE&C by courier.

**<Vendor Documents for Inspection & Tests Procedure and Quality Control >**

Addressee : OIEC (Detail Engineering Company)
CC : LGE&C (PURCHASER)

C : Vendor to transmit Vendor Documents for inspection & tests procedure and Quality Control Plan to OIEC by courier in compliance with Para. 2.3
C' : In parallel with C, VENDOR to distribute three (3) copies of Vendor Documents transmitted by C, with VPCS to LGE&C by courier.
D : LGE&C to make his comments on Vendor Documents for Inspection transmitted by C', and inform OIEC of the comments by facsimile or courier in time(within Max. 10 days)

E : OIEC to return one(1) copy of Vendor Documents transmitted by C, with CONSORTIUM's checking result to VENDOR by courier.

E' : In parallel with E, OIEC to distribute one (1) copy of checked Vendor Documents to LGE&C by courier.

**<Vendor Documents for Packing & Shipping and Schedule & Progress Monitoring >**

Addressee : LGE&C (PURCHASER)

CC : OIEC (Detail Engineering Company)

F : Vendor to transmit Vendor Documents for packing & shipping and schedule & progress monitoring to LGE&C by Courier in compliance with Article 2.3
by courier, because checking and return of these Vendor Documents are PURCHASER's responsibility.

F' : In parallel with F, VENDOR to distribute one(1) copy of Vendor Documents transmitted by F, with VPCS to OIEC by courier.


G : OIEC to make his comments on Vendor Documents for packing & shipping and schedule & progress monitoring transmitted by F', and inform LGE&C of his comments by facsimile or courier in time.

H : LGE&C to return one(1) copy of Vendor Documents transmitted by F, with CONSORTIUM's checking result to VENDOR by courier.

H' : In parallel with H, LGE&C to distribute one(1) copy of checking results to OIEC by courier.

**2) If PURCHASER is OIEC and Detail Engineering Co. is LGE&C (Req. No. ; LG*****),**

Documents shall be submitted as follows ;

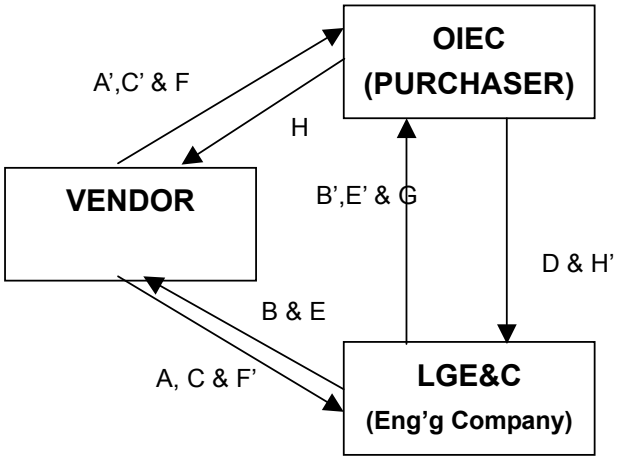


Note :
Inspection Documents include; QC Plan, WPS/PQR, Inspection Procedure, NDE Procedure, Hydrostatic Test Procedure, PWHT Procedure, Manufacturing Data Record (MDR), Fabrication Procedure, and so on

**<Technical Vendor Documents>**
Addressee : LGE&C (Detail Engineering Company)
CC : OIEC (PURCHASER)

A : VENDOR to transmit Vendor Documents to LGE&C by courier in compliance with Para. 2.3.

A' : In parallel with A, VENDOR to distribute one (1) copy of Vendor Documents transmitted by A, with VPCS to OIEC by courier.

B : LGE&C to return one (1) copy of Vendor Documents transmitted by A, with CONSORTIUM's checking result to VENDOR by courier. In addition, LGE&C to inform VENDOR of OWNER's comments on these Vendor Documents.

B' : In parallel with B, LGE&C to distribute one(1) copy of checked Vendor Documents to OIEC by courier.

**<Vendor Documents for Inspection & Tests Procedure and Quality Control Plan>**
Addressee : LGE&C (Detail Engineering Company)
CC : OIEC (PURCHASER)

C : Vendor to transmit Vendor Documents for inspection & tests Procedure and Quality Control Plan to LGE&C by courier in compliance with Para. 2.3
C' : In parallel with C, VENDOR to distribute three (3) copies of Vendor Documents transmitted by C, with VPCS to OIEC by courier.
D : OIEC to make his comments on Vendor Documents for Inspection transmitted by C', and inform LGE&C of the comments by facsimile or courier in time(within Max. 10 days)
E : LGE&C to return one(1) copy of Vendor Documents transmitted by C, with CONSORTIUM's checking result to VENDOR by courier.
E' : In parallel with E, LGE&C to distribute one (1) copy of checked Vendor Documents to OIEC by courier.

**<Vendor Documents for Packing & Shipping and Schedule & Progress Monitoring >**

Addressee : OIEC (PURCHASER)
CC : LGE&C (Detail Engineering Company)

F : Vendor to transmit Vendor Documents for packing & shipping and schedule & monitoring to OIEC by courier in compliance with Article 2.3, because checking and return of these Vendor Documents are PURCHASER's responsibility.

F' : In parallel with F, VENDOR to distribute one(1) copy of Vendor Documents transmitted by F, with VPCS to LGE&C by courier.


G : LGE&C to make his comments on Vendor Documents for packing & shipping and schedule & progress monitoring transmitted by F', and inform OIEC of his comments by facsimile or courier in time.

H : OIEC to return one(1) copy of Vendor Documents transmitted by F, with CONSORTIUM's checking result to VENDOR by courier.

H' : In parallel with H, OIEC to distribute one(1) copy of checking results to LGE&C by courier.

**3) If PURCHASER & Detail Engineering Co. is LGE&C (Req. No. ; LG*****),**

Document shall be submitted as follows ;




**<All Vendor Documents>**


A : VENDOR to transmit all Vendor Documents to LGE&C by courier in compliance with Para. 2.3.

B : LGE&C to return one (1) copy of Vendor Documents with CONSORTIUM's checking result to VENDOR by courier. In addition, LGE&C to inform VENDOR of COMPANY's comments on these Vendor Documents, if necessary.

B' : In parallel with B, LGE&C to distribute one(1) copy of checked Vendor Documents to OIEC by courier.

**4) If PURCHASER & Detail Engineering Co. is OIEC (Req. No. ; OI*****),**

Document shall be submitted as Follows ;




**<All Vendor Documents>**

A : VENDOR to transmit all Vendor Documents to OIEC by courier in compliance with Article 2.3.

B : OIEC to return one (1) copy of Vendor Documents with CONSORTIUM's checking result to VENDOR by courier. In addition, OIEC to inform VENDOR of COMPANY's comments on these Vendor Documents, if necessary.

B' : In parallel with B, OIEC to distribute one (1) copies of checked Vendor Documents to LGE&C by courier.

**ATTACHMENT #3**

## STANDARD FORMS

| | | |
|---|---|---|
| FORM 1 | : | Vendor Print Control Sheet (VPCS) |
| FORM 2 | : | Vendor Print Index & Schedule (VPI) |
| FORM 3 | : | Overall Manufacturing Schedule / Detail Production Schedule |
| FORM 4 | : | Sub-order Status Report |
| FORM 5 | : | Vendor Personnel/Organization |
| FORM 6 | : | Monthly Progress Reports |
| ***FORM 7*** | ***:*** | ***Electric Load List*** |
| ***FORM 8*** | ***:*** | ***Lubricant List*** |
| ***FORM 9*** | ***:*** | ***Utility Consumption List*** |
| ***FORM 10*** | ***:*** | ***SPIR Format*** |
| ***FORM 11*** | ***:*** | ***Special Tool List*** |

# Overall Manufacturing Schedule / Detail Production Schedule

**FORM 3**

**Project Name : SP 9&10 Project**

**Req. No.:**

| TIME SCHEDULE / ITEM | | |

# SUB-ORDER STATUS REPORT

**FORM 4**

**WORK NO.** **POGC-760-81-156**
**PROJECT NAME** **SP 9&10 Project**
**REQ NO.** _____
**ITEM NO.** _____
**DESCRIPTION** _____
**DELIVERY DATE** *(FOB/CFR/ )*

**VENDOR :** _____
**PERSON IN CHARGE:** _____
**TEL NO. :** _____
**FAX NO. :** _____
**CHK'D DATE :** _____

| DESCRIPTION OF SUB-ORDER | TYPE AND GRADE OF MATERIAL | ISSUED DATE OF B.M | VENDOR'S | | | ARRIVAL DATE AT VENDOR'S SHOP | | | REMARKS |
|---|---|---|---|---|---|---|---|---|---|
| | | | P/O NO. & ISSUED DATE | NAME & LOCATION OF SUB-VENDOR | PERSON IN CHARGE<br>TEL.NO.<br>FAX.NO. | REQ'D | CURRENT ESTIMATE | ACTUAL | |
| | | | | | | | | | |
| | | | | | | | | | |
| | | | | | | | | | |
| | | | | | | | | | |

# VENDOR PERSONNEL/ORGANIZATION

WORK NO. : POGC-760-81-156 **FORM 5**

SP 9&10 PROJECT

REQ.NO.

VENDOR :

ADDRESS :

PHONE NO : FAX NO. : e-mail :

PERSON IN CHARGE (PROJECT MANAGER) :

| ACTIVITY | DEPARTMENT | MANAGER | PERSON IN CHARGE | PHONE NO. |
|---|---|---|---|---|
| SALES<br>EXPEDITING | | | | |

MANUFACTURER :

ADDRESS :

PHONE NO : FAX NO. : e-mail :

PERSON IN CHARGE (PROJECT MANAGER) :

| ACTIVITY | MNAGER | PERSON IN CHARGE PHONE NO. e-mail |
|---|---|---|
| SALES | | |
| EXPEDITING | | |
| DESIGN | | |
| PRODUCTION | | |
| INSPECTION | | |
| DELIVERY | | |

PACKING COMPANY :

ADDRESS. :

PHONE NO : FAX NO. : e-mail :

PERSON TO CONTACT : e-mail :

FREIGHT TORWARDER :

ADDRESS :

PHONE NO : FAX NO. : e-mail :

PERSON TO CONTACT : e-mail :

NOTE: DOCUMENTS SHALL BE ADDRESSED TO :

(1) FOR COMMERCIAL :

(2) FOR TECHNICAL :

(3) FOR SCHEDULE :

# MONTHLY PROGRESS REPORT

**FORM 6**

Work No. POGC-760-81-156,

SP 9&10 Project Date : _____

| | | |
|---|---|---|
| Req. No. | Item No. | |
| P/O No. | Description : | |
| Delivery Condition | Delivery Date : | dd mm yy |
| Location : | Contractual | as of |
| FOB / FCA / EWX / DDU / | Last Promised | as of |
| | Present Estimate | as of |

This report covers Progress for the period of _____ - _____

(start) - (end)

1. Major Activities in the month :

| 2. Progress and Current Estimate | Weight Factor (%)* | Scheduled (Origianl Plan) | | Actual Status & Current Estimate | | | Remark |
|---|---|---|---|---|---|---|---|
| | | Start (dd/mm/yy) | Complete (dd/mm/yy) | Start (dd/mm/yy) | Progress (%)* | Complete (dd/mm/yy) | |
| 1) Design / Engineering | | | | | | | |
| 2) Materials / Sub-order | | | | | | | |
| Materials / receipt | | | | | | | |
| 3) Production | | | | | | | |
| 4) Inspection and Tests | | | | | | | |
| 5) Shipping Preparation | | | | | | | |
| 6) Inland Transportation | | | | | | | |
| Overall | 100 | --- | --- | --- | | --- | |

*Note : Overall Progress shall be Sum of [Weight Factor] x [ Progress]. Weight Factor shall be set by Vendor.

| Cumulative Progress (%) | | | | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | Month | | | | | | | | | | | | | |
| | Plan | | | | | | | | | | | | | |
| | Actual | | | | | | | | | | | | | |

3. Major Activities for Next Month:

4. Attachment ☐ Fabrication schedule ☐ Sub-Order Status Report

☐ Other Document
